Scope Management Plan
Repairo - Instrument Repair Management & Tracking System

CIS 4524
Lake Baldwin Music Academy
Prepared By: Harmonic Solutions
Date: 6/21/25

---

1. ***Project Information:***

Project Name:

- Repairo - Instrument Repair Management & Tracking System

Team Name:

- Harmonic Solutions

Team Members:

Project Manager:

- Marcos Rivera

Team Members:

- Zahrah Ali, Lindsey Duong, Glory Mathew, and Nicole Walsh

---

2. ***Project Description:***

After Lake Baldwin Music Academy's decision to move forward with a custom information system, the Harmonic Solutions team will take the next steps in the Repairo project to develop a comprehensive system tailored

specifically for our instrument repair management needs. Working underneath Lake Baldwin Music Academy, our team has been entrusted with the responsibility of maintaining inventory on repairs and conducting these repairs ourselves. The Repairo system will transition LBMA from their current paper-based management system to a digital software solution.

---

3. <u>Project MOV:</u>

a. Desired Areas of Impact (Ranked by Importance)

1. **Operational -** Streamlines repair processes and inventory management.
2. **Customer -** Improves quality of service and response times on repairs, introduces repair status tracking for students and parents of LBMA.
3. **Financial -** Reduces operational costs, improves revenue through more efficient repairs.
4. **Strategic -** Positions LBMA as a forward-thinking institution to attract more people.
5. **Social -** Supports musical education and the academy's community via a reliable instrument repair system.

b. Desired Value of the IT Project

<u>Primary Value This Project Offers:</u>

- **Efficiency -** Reduction in instrument repair cycles with more responsive repair requests and automated updates.
- **Quality -** We'll enhance service quality through an improved tracking system and through automated processes.
- **Accuracy -** Less room for errors and/or losing of paperwork.
- **Enhanced Security -** Only authorized users can access this.

c. *Appropriate Metrics*

- *Operational Efficiency:* Reduce average repair cycle from 14 days to 5-7 days.
- *Customer Satisfaction:* Achieve 95% or greater customer satisfaction rating for repair services.
- *Cost Reduction:* Decrease repair operational costs by at least 25% or greater.
- *System Accessibility:* Achieve 99.5% system uptime during business operating hours.

d. *Time Frame for Achieving MOV*

Phase 1:

- 6 months after project start: Complete system implementation

Phase 2:

- 9 months after project start: Achieve 50% of targeted improvements as staff adapts to new processes

Phase 3:

- 12 months after project start: Achieve 75% of targeted improvements with optimized workflows.

Phase 4:

- 18 months after project start: Achieve full MOV targets with mature system utilization.

e. *MOV Summary Statement*

This project will prove to be successful if Lake Baldwin Music Academy reduces instrument repair cycle times from the typical 14 days down to 5-7 days, customer satisfaction for repair services are at or above a 95% threshold, LBMA decreases repair-related operational costs by 25%, and maintains 99.5% system uptime, all of these met within 12 months of the new system implementation.

---

4. ***Deliverable Structure Chart (DSC):***

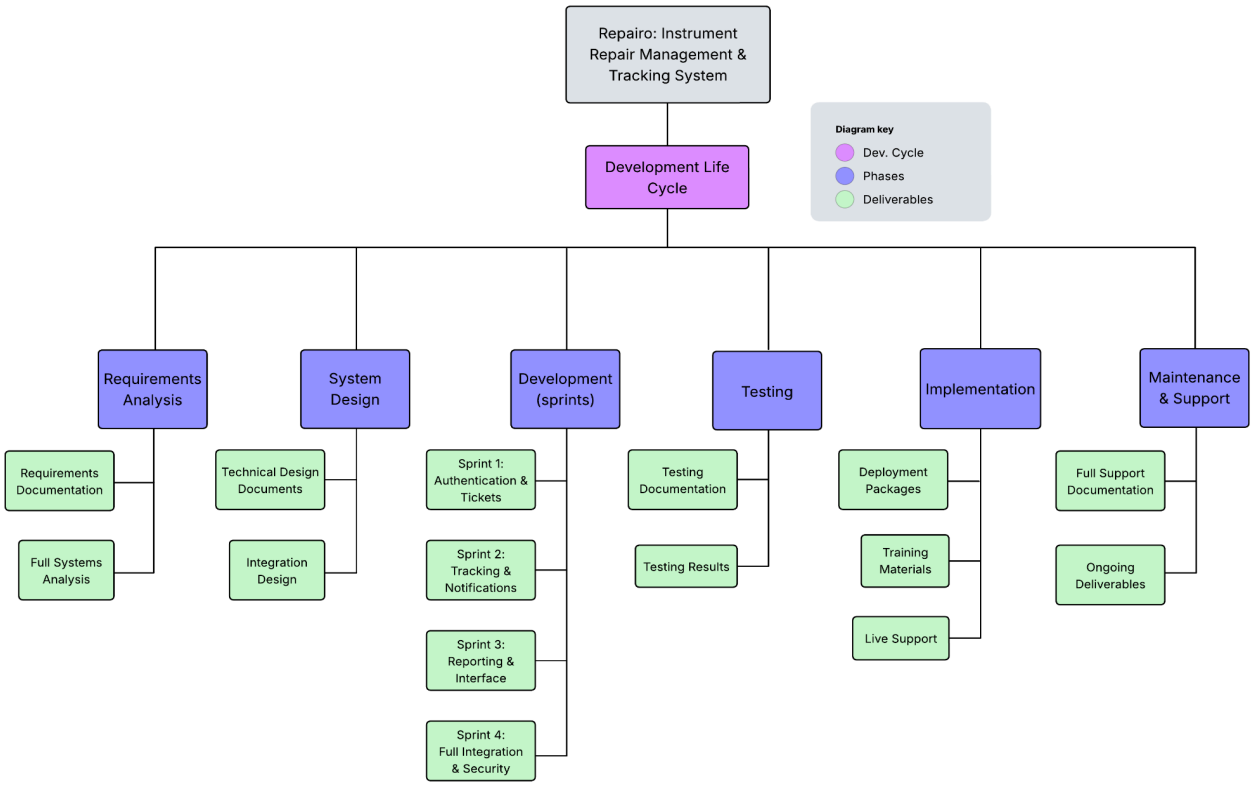

5. ***Use Case Diagram (UCD):***

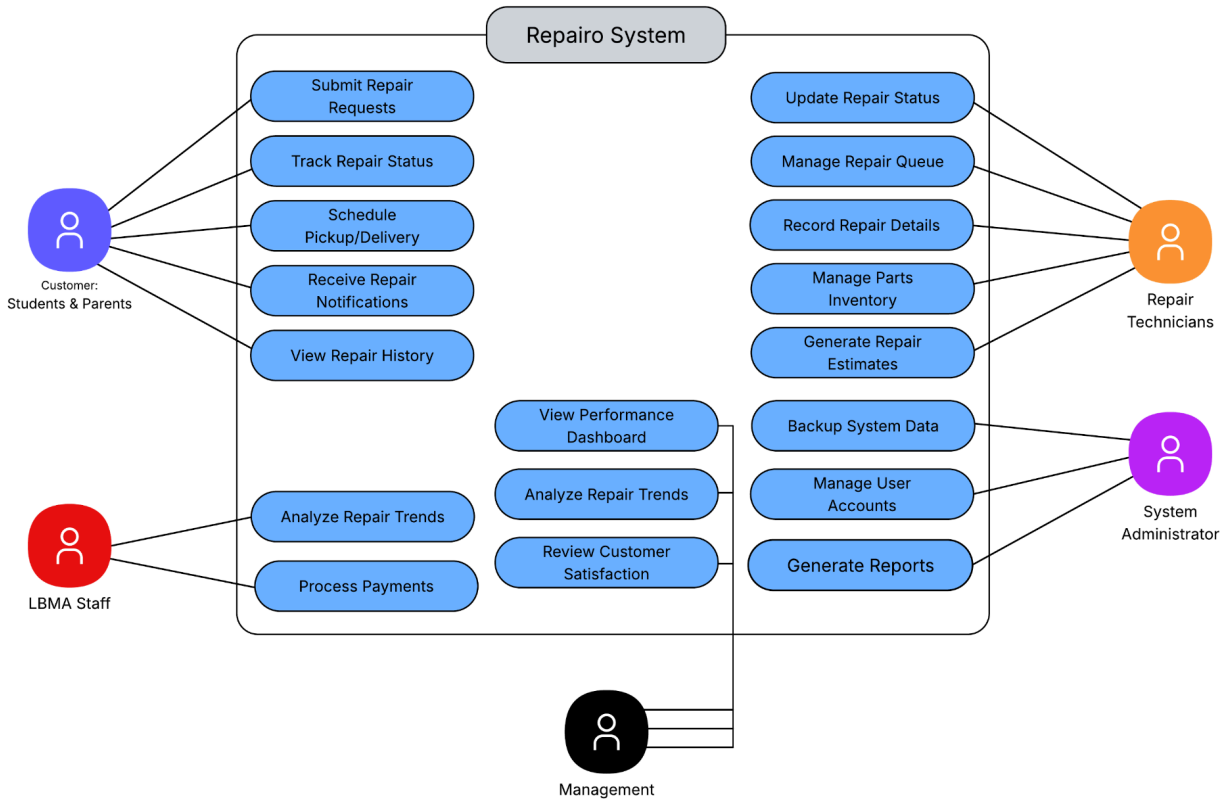

6. ***Scope Change Process:***

Scope Change Management Overview:

The scope change process can ensure that any modifications to the project scope are thoroughly evaluated, approved, and implemented all in a controlled manner.

ALL scope changes must be documented, assessed, and approved before implementation.

Steps for Scope Change Process:

Step 1: Identify Change Request

- **Trigger:** Any stakeholder identifies a need for scope modification.
- **Action:** Complete Scope Change Request Form. (SCR-1)
- **Responsibility:** Requesting party.

Step 2: Initial Assessment

- **Timeline:** Within 2 business days of request submission.
- **Action:** Project Manager conducts preliminary impact assessment.
- **Deliverable:** Initial Impact Assessment. (SCR-2)

Step 3: Initial Assessment

- **Timeline:** Within 5 business days of initial assessment.
- **Action:** Technical team conducts detailed analysis.
- **Deliverable:** Detailed Impact Analysis Report. (SCR-3)

Step 4: Change Control Board Review:

- **Participants:**
  - ➢ Project Manager (Marcos Rivera)
  - ➢ Lead Systems Analyst (Zahrah Ali)
  - ➢ LBMA Executive Sponsor
  - ➢ Key Stakeholder Representative
- **Timeline:** Within 3 business days of detailed analysis completion.
- **Decision:** Approve, Defer, or Reject.

Step 5: Implementation Planning:

- **Condition:** Only for approved changes.
- **Timeline:** Within 2 business days of approval.
- **Action:** Update project documents and communicate changes.
- **Deliverables:** Updated Project Schedule, Revised Budget Estimates, New Scope Statement, Stakeholder Communication.

Step 6: Implementation and Monitoring:

- **Action:** Execute approved changes according to the updated plan.
- **Monitoring:** Track implementation progress and impact.
- **Reporting:** Update project status reports with change impact.

Scope Change Documentation Templates:

Scope Change Request Form - (SCR-1)

SCOPE CHANGE REQUEST FORM

Request ID: SCR-[YYYY]-[###]

Date Submitted: _____

Submitted By: _____

Work Phone Number: _____

PROJECT INFORMATION

Project Name: Repairo System

Project Manager: Marcos Rivera

Current Project Phase: _____

CHANGE REQUEST DETAILS

Change Type: ☐ Addition ☐ Modification ☐ Deletion

Priority: ☐ High ☐ Medium ☐ Low

Urgency: ☐ Immediate ☐ Next Sprint ☐ Future Release

DESCRIPTION OF REQUESTED CHANGE

Proposed Change: _____

Business Justification: _____

Impact on MOV: _____

REQUESTING PARTY INFORMATION

Organization: _____

Role: _____

Signature: _____ Date: _____

Initial Impact Assessment (SCR-2)

INITIAL IMPACT ASSESSMENT

Change Request ID: SCR-[YYYY]-[###]

Assessment Date: _____

Assessed By: _____

PRELIMINARY IMPACT ANALYSIS

Schedule Impact: ☐ None ☐ Minor ☐ Moderate ☐ Significant

Budget Impact: ☐ None ☐ Minor ☐ Moderate ☐ Significant

Resource Impact: ☐ None ☐ Minor ☐ Moderate ☐ Significant

Risk Level: ☐ Low ☐ Medium ☐ High

ESTIMATED IMPACTS

Time: +/- ___ days

Cost: +/- $___

Resources: _____

RECOMMENDATION

☐ Proceed with Detailed Analysis

☐ Request Additional Information

☐ Recommend Rejection

Project Manager Signature: _____ Date: _____

Detailed Impact Analysis Report (SCR-3)

INITIAL IMPACT ASSESSMENT

Change Request ID: SCR-[YYYY]-[###]

Analysis Date: _____

Analyzed By: _____

TECHNICAL IMPACT ANALYSIS

Development Impact: _____

Testing Impact: _____

Integration Impact: _____

SCHEDULE IMPACT

Current Milestone Dates: _____

Revised Milestone Dates: _____

COST IMPACT

Additional Development & Testing Hours: ____

Additional Resources Required: ____

Total Estimated Cost: $____

RECOMMENDATION

☐ Approve as Requested

☐ Approve with Modifications

☐ Defer to Future Phase

☐ Reject

Analyst Signature: _____ Date: _____
